

Transforming lives through excellent education

JPS Board of Trustees Bond Update January 5, 2021



JACKSON PUBLIC SCHOOLS

Presentation Overview

- Phase I & II Construction Updates
- Bond Financial Report Update
- Bond Communications Update

Bond Construction Program Phase I Project Updates Murrah High School

Construction Phase

- Restroom Renovations
- Science Lab Renovations
- Entry and Site Walkway Repairs






Murrah High School







Murrah High School

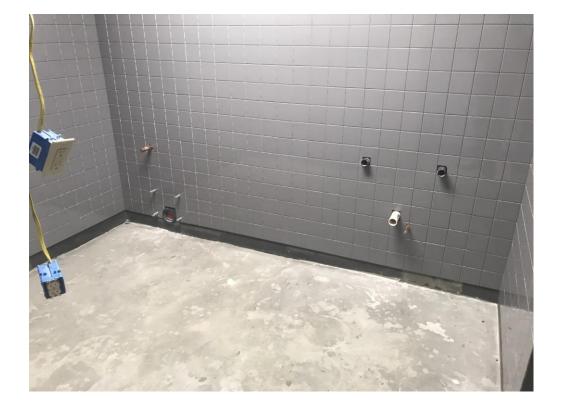





Provine High School

- **Construction Phase**
- Restroom Renovations
- Science Lab Renovations
- Kitchen Plumbing Repairs
- Parking Lot Repair





Provine High School

Kitchen Plumbing Replacement







Provine High School

Parking Lot Repairs

BEFORE

AFTER



Wingfield High School

Construction Phase

- Structural Repairs
- Science Lab Upgrades
- Library and Academy Renovations
- Exterior Door Replacements





Capital City Alternative School

Site Drainage and Foundation Repair

BEFORE



AFTER







Capital City Alternative School





Capital City Alternative School

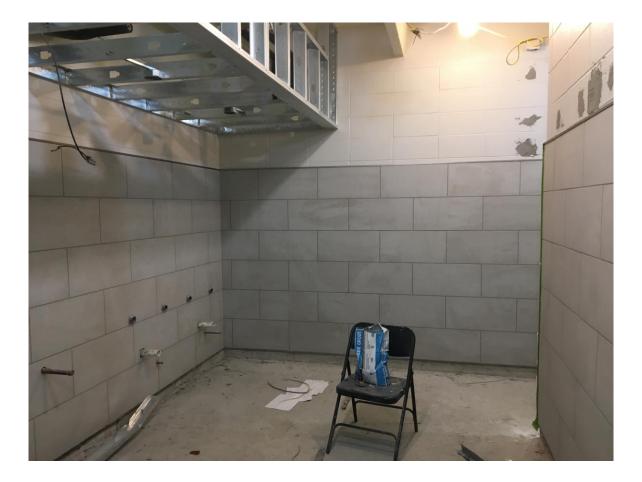

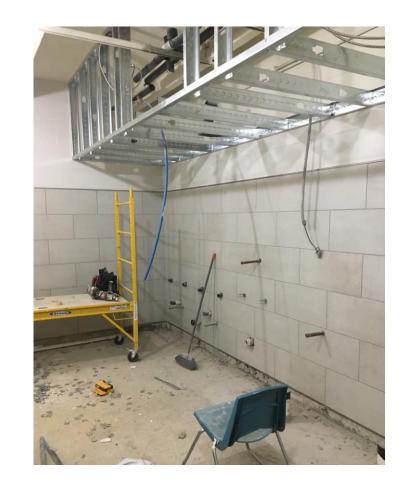



Lanier High School





Jim Hill High School

Construction Phase

- Restroom Renovations
- Gym Improvements
- Science Lab Upgrades
- Library Upgrades





Callaway High School

Construction Phase

• Infrastructure







Callaway High School

New Windows – MDE Requirement



BEFORE





High School Libraries and Academies

*Construction Phase*Forest Hill High School






High School Libraries and Academies


Forest Hill High School





Green Elementary School

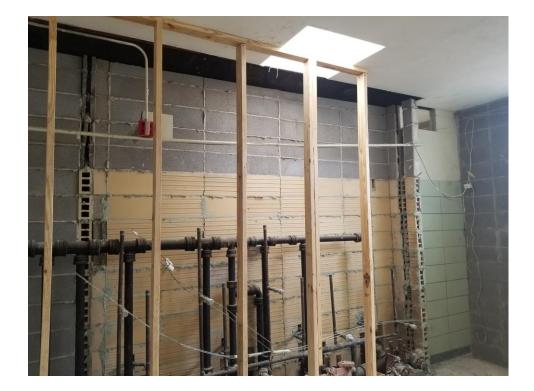

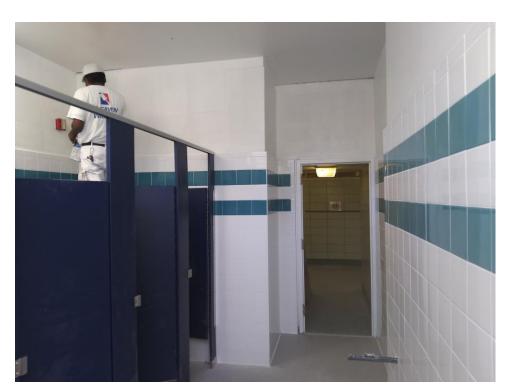



Bond Financial Update as of December 18, 2020

JACKSON PUBLIC SCHOOLS 2018 BOND FUND SCHEDULE OF BUDGET BALANCES						
	{A}	{B}	{C}	D={A-B-C}		
SCHOOL/SITE	Budget	Expenditures	Encumbered	Budget Balance		
Bailey	1,226,000.00	65,872.76	24,527.24	1,135,600.00		
Baker	260,000.00	1,880.00	12,120.00	246,000.00		
Bates	270,000.00	23,800.00		246,200.00		
Blackburn	706,000.00	2,366.42	71,846.58	631,787.00		
Boyd	330,000.00	249,476.41	53,441.25	27,082.34		
Brinkley	1,146,000.00	35,101.92	71,185.08	1,039,713.00		
Callaway	7,409,600.00	6,054,785.88	1,261,984.97	92,829.15		
Capital City	811,809.43	244,850.96	248,169.04	318,789.43		
Cardozo	646,000.00	34,176.56	23,523.44	588,300.00		
Career Development Center	500,000.00	417,779.05	59,819.25	22,401.70		
Casey	230,000.00	124,327.22	54,145.71	51,527.07		
Chastain	1,076,000.00	58,020.64	67,032.56	950,946.80		
Clausell	320,000.00	5,120.00	20,480.00	294,400.00		
Dawson	225,000.00	1,640.00	13,360.00	210,000.00		
Forest Hill	10,753,150.00	4,840,205.16	1,737,719.41	4,175,225.43		
Galloway	280,000.00	71,114.69	20,000.00	188,885.31		
Green	1,000,000.00	604,222.92	<u>391,915.88</u>	3,861.20		
Hardy	730,000.00	266,675.92	311,041.56	152,282.52		
Isable	210,000.00			210,000.00		
Jim Hill	2,998,400.00	554,741.75	1,375,201.44	1,068,456.81		
John Hopkins	860,000.00	41,828.10	48,240.00	769,931.90		
Johnson	350,000.00	8,824.00	19,176.00	322,000.00		
Кеу	190,000.00	44,033.90	8,640.00	137,326.10		




JACKSON PUBLIC SCHOOLS 2018 BOND FUND SCHEDULE OF BUDGET BALANCES							
	{A}	{B}	{C}	D={A-B-C}			
SCHOOL/SITE	Budget	Expenditures	Encumbered	Budget Balance			
Kirksey	511,000.00	699.38	23,300.62	487,000.00			
Lake	480,000.00			480,000.00			
Lanier	2,829,327.06	440,356.74	1,475,728.60	913,241.72			
Lee	305,000.00	29,797.55	19,520.00	255,682.45			
Lester	530,000.00	3,840.00	36,160.00	490,000.00			
Marshall	430,000.00	45,662.74	27,520.00	356,817.26			
McLeod	510,000.00			510,000.00			
McWillie	150,000.00	1,828.60		148,171.40			
Morrison	190,000.00			190,000.00			
Murrah	2,775,447.64	652,581.84	1,131,009.38	991,856.42			
North Jackson	290,000.00	6,637.50	17,880.00	265,482.50			
Northwest	1,126,000.00	69,832.00	79,136.26	977,031.74			
Oak Forest	780,000.00	6,240.00	59,193.85	714,566.15			
Obama Magnet	170,000.00	101,694.37	7,278.22	61,027.41			
Pecan Park	530,000.00	29,175.00	38,160.00	462,665.00			
Peeples	756,000.00	7,521.60	16,478.40	732,000.00			
Powell	1,107,217.00	160,997.79	58,542.94	887,676.27			
Power APAC	1,530,000.00	12,240.00	110,160.00	1,407,600.00			
Provine	2,864,261.93	921,346.35	1,014,483.39	928,432.19			
Raines	1,100,000.00	16,250.00	71,750.00	1,012,000.00			
Rowan	200,000.00			200,000.00			
Smith	330,000.00			330,000.00			



JACKSON PUBLIC SCHOOLS 2018 BOND FUND SCHEDULE OF BUDGET BALANCES							
	{A}	{B}	{C}	D={A-B-C}			
SCHOOL/SITE	Budget	Expenditures	Encumbered	Budget Balance			
Sykes	280,000.00			280,000.00			
Timberlawn	330,000.00	91,965.00		238,035.00			
Van Winkle	392,532.08	391,387.23	1,144.85	0.00			
Walton	305,000.00	4,120.00		300,880.00			
Watkins	280,000.00	1,920.00	8,080.00	270,000.00			
Whitten	1,226,000.00	28,325.04	72,832.66	1,124,842.30			
Wilkins	380,000.00	87,809.41	6,107.55	286,083.04			
Wingfield	2,525,447.65	309,499.69	1,120,141.87	1,095,806.09			
Newell Field	5,000,000.00			5,000,000.00			
Baseball/Softball Complex	1,000,000.00	28,857.30	51,142.70	920,000.00			
Hughes Field	2,300,000.00	112,658.51	117,341.49	2,070,000.00			
North Jackson Field	800,000.00	80,774.87	74,572.78	644,652.35			
South Jackson Field	565,031.00	28,691.49	536,339.51	-			
Project Management Support	600,000.00	176,719.40	10,275.60	413,005.00			
Bond Issuance Fees	346,250.00	346,250.00		-			
Un-Allocated	1,563,776.21			1,563,776.21			
Total	70,346,250.00	18,093,336.52	12,081,334.03	40,171,579.45			



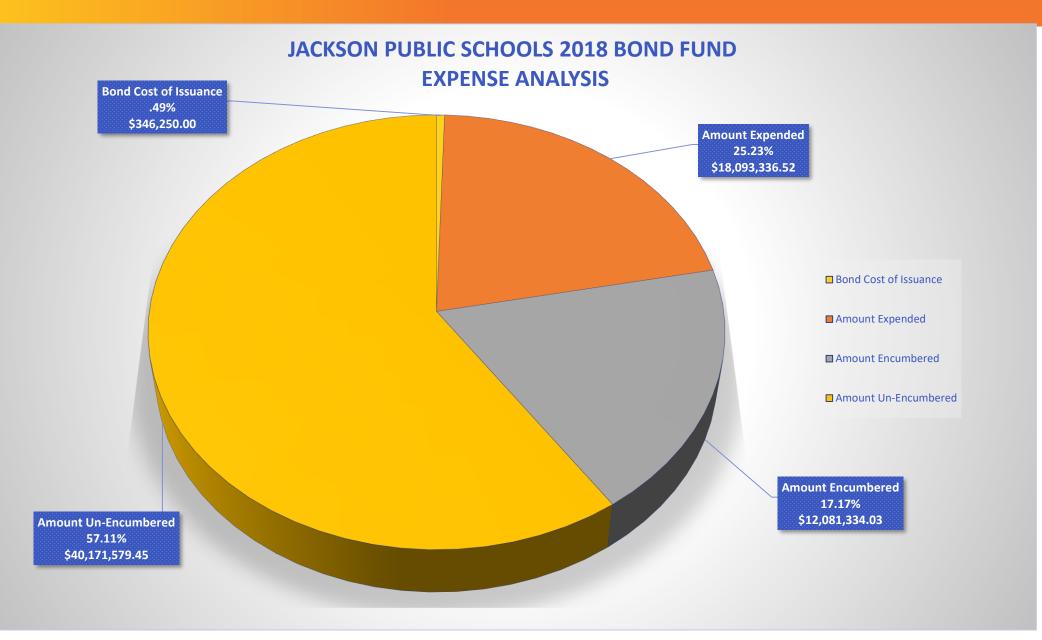



Note: Amount "Expended + Encumbered" increased from 40% to 42% since last Bond Update. Purchase orders to be issued this week total \$3,590,578.83. Amount will then be 48%.

Bond Communications Update

Social Media School of the Week Highlight

> Video Tapings of Construction Progress

Project Updates on School's Webpage



Social Media School of the Week Highlights

Weekly Posts Each Friday


- Lanier High School
- Callaway High School
- **Green Elementary School**



Jackson Public Schools January 1 at 10:49 AM · 🕥

At Green Elementary School, contractors are completing #JPSBond projects including renovating restrooms, removing carpet, replacing entry doors, building a playground canopy, and repairing sidewalks. Keep up with our progress at www.jackson.k12.ms.us/JPSBond.

...

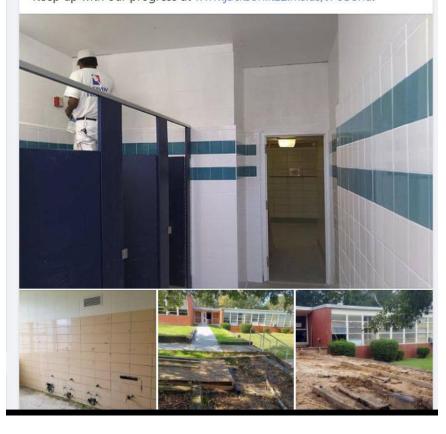



Bond Communications Update

> Video Tapings of Construction Progress


- Provine, CDC, Wingfield, Capital City, Van Winkle and Forest Hill were taped before the Winter Break and will begin airing by January 11, 2021.
- Spann will begin taping within the next two weeks.



Project Updates on School's Webpage

Green Elementary School

Bond Construction Program Project Listing and Status

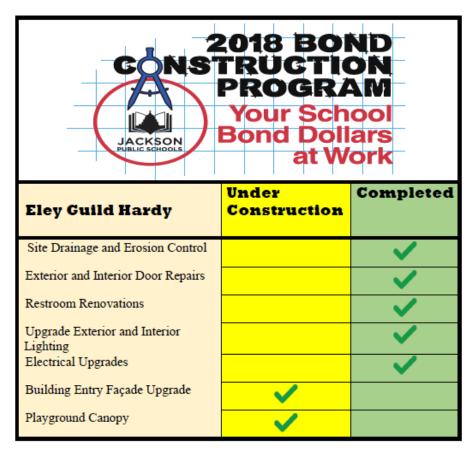



Updated as of 1/1/2021

Project Updates on School's Webpage

Green Elementary School



Exterior Door Repair Before



Exterior Door Repair After



Classroom Renovation Before

A B C D L P C E LI J L E R O P O L D T D V L Y Z

Classroom Renovation After



Exterior Railing Painting Before



Exterior Railing Painting After







Restroom Renovation Before



Transforming lives through excellent education

Thank You

We Welcome Any Questions
